# PROGRESS UPDATE #3 FLINT EAST BOULEVARD FORMER MGP SITE



#### Work completed between 6/6/2017 and 6/24/2017 includes the following:

- Continued receiving and mixing of cap materials.
- Continued dredging activities at the upstream end of the Work Area (see Picture No. 1). Instream dredging has occurred from the upstream extent of dredging to station (STA) 7+00, while bank removal has occurred from the upstream extent of dredging to STA 12+00. Design removal elevations have not yet been achieved.
- Dredged sediments were mixed with dewatering amendment in a dewatering pad, and dewatered sediment was loaded into haul trucks for disposal at the approved landfill for the project.
- Continued collection of construction monitoring data including air, odor and construction noise monitoring; turbidity monitoring; and, structural monitoring (see Picture No. 2).
- Treatment of decant water from dredged sediment through the wastewater treatment system.
- Inspection of Work Area barriers, absorbent booms, and turbidity controls on a daily basis (see Picture No. 3).
- Initial surveying activities to verify that dredging has been completed to the design dredge surface (see Picture No. 4).

#### **Upcoming work includes the following:**

- Continue instream dredging and bank removal activities.
- Continue to mix cap materials.
- Continue to collect construction monitoring data.
- Achieve final design elevations between the upstream extent of dredging and STA 7+00 and begin capping activities.
- Begin demolition of the Pedestrian Bridge.

Picture No. 1.

Dredging activities near the upstream end of the Work Area (photo taken facing north).




Picture No. 2.

Air monitoring adjacent to dredging and offloading activities (photo taken facing southwest).



Picture No. 3.

Upstream river closure barrier (photo taken facing south).

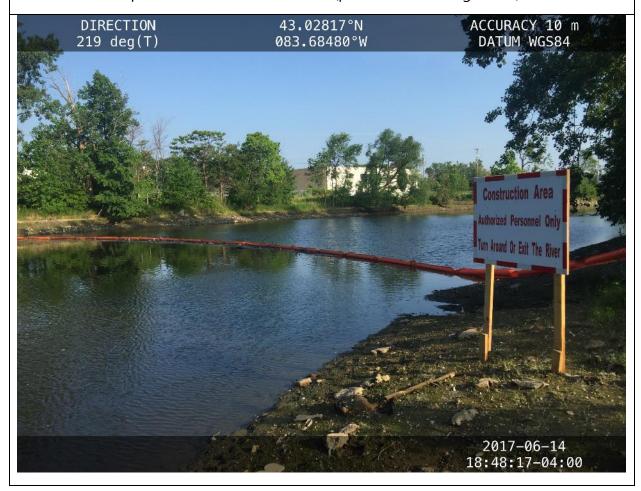

Picture No. 4. Initiating surveying activities using a Z-boat (photo taken facing west).

