

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 7/27/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc. ProAct	Contractor(s) Rep:	John Johnson (Ryan Central) Guillermo Arredondo (ProAct)

SITE CONDITIONS	
Weather (AM): Mostly Sunny	Temperature: 68
Weather (PM): Partly Cloudy	Temperature: 80
Precipitation: None	Wind: SW 3-16 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; Haul truck; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 1-Komatsu PC360LC Long Reach Excavator; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION																																																								
Work performed while Golder was onsite:																																																								
Ryan Central -2 Foreman, 4 Operators, 1 Laborer																																																								
<ul style="list-style-type: none"> Continued placement of bridging layer in Pond 2. Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Began regrading CCR in Pond 2. Received delivery of structural fill material from off-site source for Pond 1. Water truck for dust control and fill moisture. 																																																								
<u>Summary of Dewatering through 07-08-19:</u>																																																								
<table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table> <table> <thead> <tr> <th><u>Week 5</u></th> <th><u>Week 6</u></th> <th><u>Week 7</u></th> <th><u>Week 8</u></th> </tr> </thead> <tbody> <tr> <td>06/03/19: 185,365 gal.</td> <td>06/10/19: 175,022 gal.</td> <td>06/17/2019: 247,813 gal.</td> <td>06/24/2019: 218,008 gal.</td> </tr> <tr> <td>06/04/19: 409,662 gal.</td> <td>06/11/19: 184,365 gal.</td> <td>06/18/2019: 68,510 gal.</td> <td>06/25/2019: 208,371 gal.</td> </tr> <tr> <td>06/05/19: 345,122 gal.</td> <td>06/12/19: 178,934 gal.</td> <td>06/19/2019: 215,872 gal.</td> <td>06/26/2019: 181,215 gal.</td> </tr> <tr> <td>06/06/19: 311,007 gal.</td> <td>06/13/19: 147,219 gal.</td> <td>06/20/2019: 207,117 gal.</td> <td>06/27/2019: 216,650 gal.</td> </tr> <tr> <td>06/07/19: 276,790 gal.</td> <td>06/14/19: 13,156 gal.</td> <td>06/21/2019: 200,874 gal.</td> <td>06/28/2019: 208,921 gal.</td> </tr> <tr> <td>06/08/19: 65,064 gal.</td> <td>06/15/19: 142,063 gal.</td> <td>06/22/2019: 102,207 gal.</td> <td>06/29/2019: 135,907 gal.</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None	<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>	06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.	06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.	06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.	06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.	06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.	06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																																																					
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																																																					
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																																																					
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																																																					
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																																																					
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																																																					
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																																																					
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>																																																					
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.																																																					
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.																																																					
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.																																																					
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.																																																					
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.																																																					
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.																																																					

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
Total: 13,838,510 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in single lift using CCR in Pond 2.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder observed regrading of CCR in the western half of Pond 2.
- Golder observed import of structural fill for Pond 1.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature: 

PHOTOGRAPHS

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Compacting placed structural fill in Pond 1, looking northwest.



Placing structural fill in Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Placing bridging layer in Pond 2, looking west.



Removing saturated material from Pond 2 prior to bridging layer being placed.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW

Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 7/29/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc. ProAct	Contractor(s) Rep:	John Johnson (Ryan Central) Guillermo Arredondo (ProAct)

SITE CONDITIONS

Weather (AM): Mostly Sunny	Temperature: 68
Weather (PM): Mostly Cloudy	Temperature: 84
Precipitation: None	Wind: SW 5-17 mph

EQUIPMENT ON SITE

1-Kubota RTV X112OD; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 1-Komatsu PC360LC Long Reach Excavator; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION

Work performed while Golder was onsite:

Ryan Central -2 Foreman, 6 Operators, 2 Laborers

- Continued placement of bridging layer in Pond 2.
- Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift.
- Continued compacting structural fill placed in Pond 1 with an 815 compactor.
- Completed clean-up of area west of Pond 2 containing contaminated soils.
- Structural Fill import for Pond 1.
- Water truck for dust control and fill moisture.

ProAct Services – 1 Foreman

- ProAct onsite at 0700 to startup dewatering system in Pond 2.
- Turbidity readings were taken by ProAct every hour while pumping to discharge channel and licensed tester onsite in P.M.
- System back flushed and filters changed as needed.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

Summary of Dewatering through 07-29-19:

<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
Total: 13,838,510 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in a single layer using CCR in Pond 2.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-23 and SFDT-24 on 9-inch compacted structural fill lift's 1 and 3 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder monitored removal of contaminated soils west of Pond 2 and placement in lined dumpster, contaminated water pumped into baker tank.
- Golder observed import of structural fill for Pond 1.
- Golder observed pumping of Pond 2 thru filtering system into discharge channel.
- Golder observed use of water truck for dust control on site.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS
--

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)
--

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES
--

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature: 
--

PHOTOGRAPHS



Compacting lift of structural fill in Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Placing bridging layer in Pond 2, looking southeast.



Baker tank for holding of contaminated water until disposal off-site, looking southeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Preparing to pump contaminated water into baker tank.



Density testing compacted lift of structural fill in Pond 1, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW

Project Title: J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 7/30/2019
Client: Consumers Energy	Site/Location: Erie, MI	
GAI Personnel: David Hutchinson	Arrival/Departure Time: 0630/2000	
Contractor(s): Ryan Central Inc. ProAct	Contractor(s) Rep: John Johnson (Ryan Central) Guillermo Arredondo (ProAct)	

SITE CONDITIONS

Weather (AM): Mostly Sunny	Temperature: 68
Weather (PM): Mostly Sunny	Temperature: 90
Precipitation: None	Wind: W 0-10 mph

EQUIPMENT ON SITE

1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 1-Komatsu PC360LC Long Reach Excavator; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION

Work performed while Golder was onsite:

Ryan Central -2 Foreman, 5 Operators, 2 Laborers

- Continued placement of bridging layer in Pond 2.
- Continued regrading of CCR in Pond 2.
- Continued excavation of Pond 2's south dike and hauling material to Pond 2.
- Continued removing saturated CCR from the northeast corner of Pond 2 to dry.
- Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift.
- Continued compacting structural fill placed in Pond 1 with an 815 compactor.
- Structural Fill import for Pond 1.
- Water truck for dust control and fill moisture.

ProAct Services – 1 Foreman

- ProAct onsite at 0700 to startup dewatering system in Pond 2.
- Turbidity readings were taken by ProAct every hour while pumping to discharge channel and licensed tester onsite in A.M.
- System back flushed and filters changed as needed.
- Began breaking down hoses, pumps and filter system for demobilization.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

Summary of Dewatering through 07-30-19:

<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in a single layer using CCR in Pond 2.
- Golder observed regrading of CCR in Pond 2.
- Golder observed excavation of Pond 2's south dike, material placed into Pond 2 for use in bridging layer.
- Golder observed removal of saturated CCR from the northeast corner of Pond 2, material spread in a thin 2 inch lift to dry prior to use in bridging layer.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-25 and SFDT-27 on 9-inch compacted structural fill lift 4 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed import of structural fill for Pond 1.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

- Golder observed discharge of water in baker tanks thru filtering system and into the discharge channel.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Compacting lift of structural fill in Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Placing bridging layer in Pond 2, looking north.



Removing saturated CCR from the northeast corner of Pond 2, looking southeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Regrade of CCR in Pond 2, looking east.



CCR excavated from south dike being placed in Pond 2 for bridging layer, looking east.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 7/31/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc. ProAct	Contractor(s) Rep:	John Johnson (Ryan Central) Guillermo Arredondo (ProAct)

SITE CONDITIONS	
Weather (AM): Mostly Cloudy	Temperature: 66
Weather (PM): Partly Cloudy	Temperature: 85
Precipitation: None	Wind: E 2-9 mph

EQUIPMENT ON SITE
1-Kubota RTV X112OD; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 1-Komatsu PC360LC Long Reach Excavator; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION																												
Work performed while Golder was onsite:																												
Ryan Central -2 Foreman, 5 Operators, 2 Laborers																												
<ul style="list-style-type: none"> Removed fence around east end of the discharge channel and installed waddles. Removed the sheet pylon running under the perimeter road from the southeast corner of Pond 2 toward the south to the discharge channel. Continued placement of bridging layer in Pond 2. Continued regrading of CCR in Pond 2. Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. 																												
ProAct Services – 1 Foreman																												
<ul style="list-style-type: none"> ProAct onsite at 0700 to completed breakdown of the filter system for repositioning. 																												
<u>Summary of Dewatering through 07-31-19:</u>																												
<table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																									
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																									
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																									
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																									
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																									
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																									
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																									

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in a single layer using CCR in Pond 2.
- Golder observed regrading of CCR in Pond 2.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-28 and SFDT-30 on 9-inch compacted structural fill lift 4 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed import of structural fill for Pond 1.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Removing sheet pylon east of Pond 2 and discharge channel, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Compacting lift of structural fill placed in Pond 1, looking northeast.



Removing fence along east side of discharge channel, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure




Overview of Pond 2, looking west.



Structural fill import for Pond 1, looking east.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

DENSITY TEST MAP LIFT 2

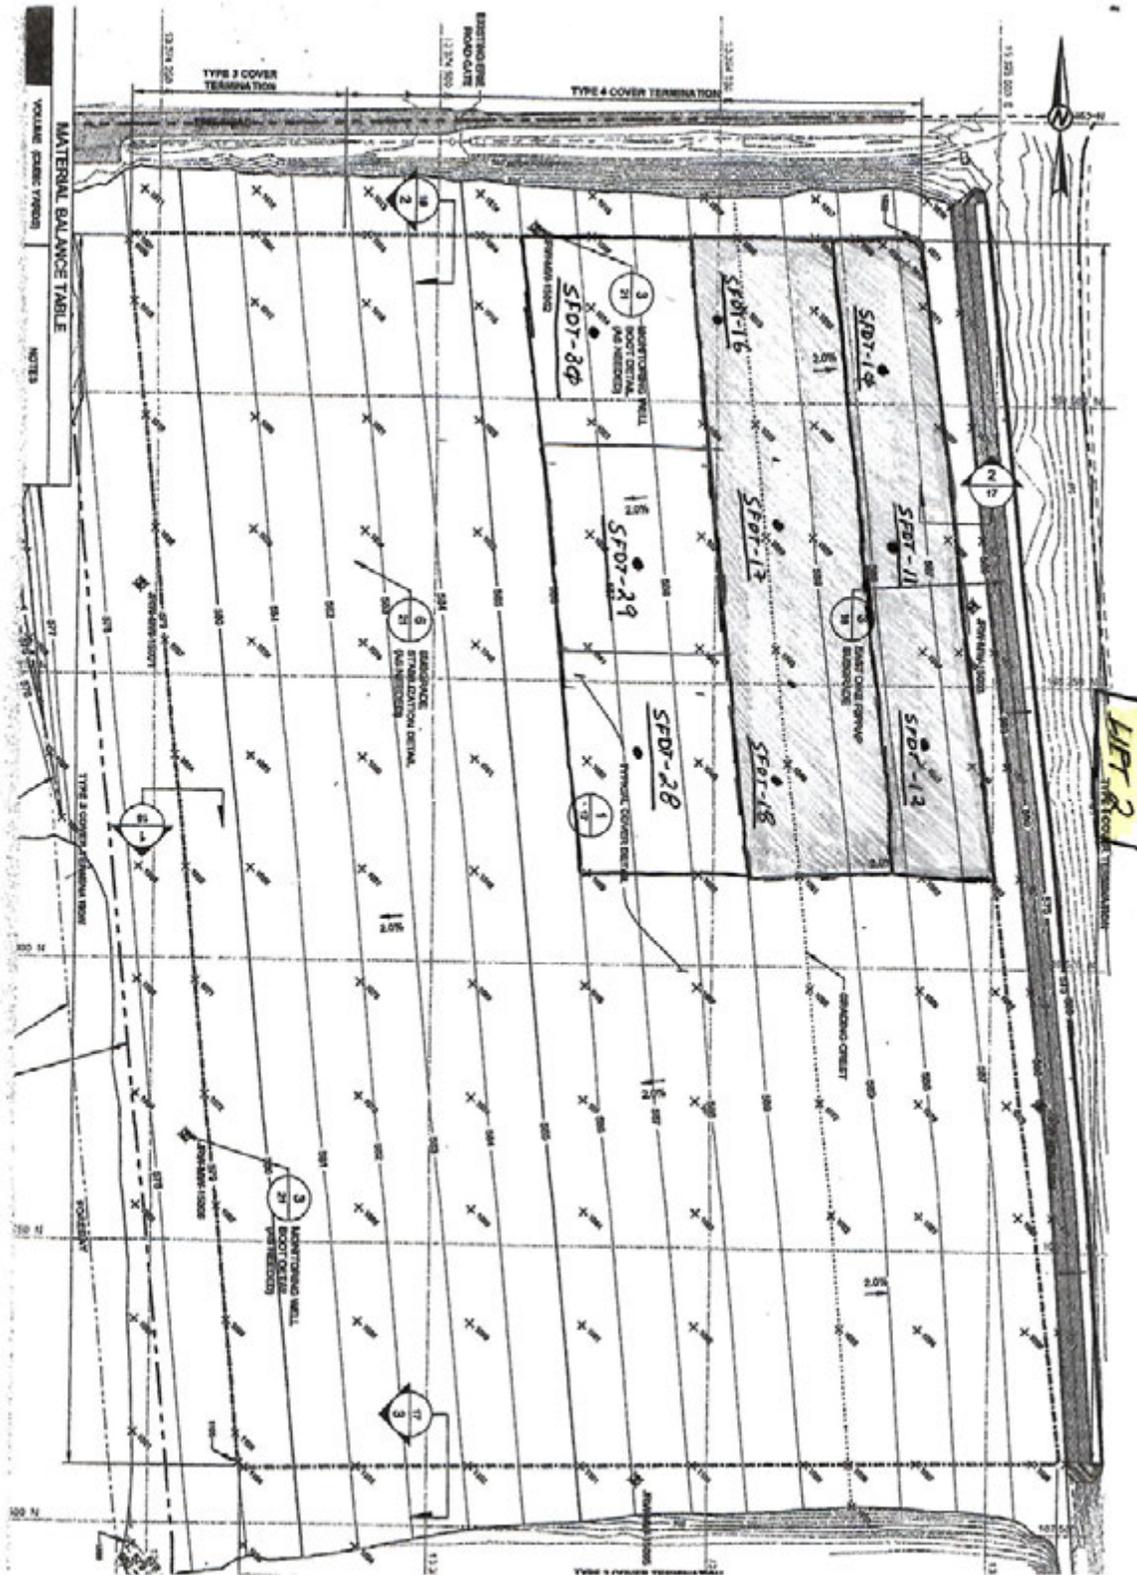

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/1/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Mostly Sunny	Temperature: 61
Weather (PM): Sunny	Temperature: 81
Precipitation: None	Wind: W 0-6 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION	
Work performed while Golder was onsite:	
Ryan Central -2 Foreman, 5 Operators, 2 Laborers	
<ul style="list-style-type: none"> Continued placement of bridging layer in Pond 2. Continued regrading of CCR in Pond 2. Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Continue excavating Pond 2's south dike and placing material into Pond 2 for bridging layer. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. Demobilized Komatsu PC360LC Long Reach Excavator 	
<u>Summary of Dewatering through 07-31-19:</u>	
<u>Week 1</u>	<u>Week 2</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.
<u>Week 3</u>	<u>Week 4</u>
05/20/19: 328,687 gal.	05/27/19: Holiday
05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.
<u>Week 7</u>	<u>Week 8</u>
06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PHOTOGRAPHS



Excavation of Pond 2's south dike, looking southeast.



Placement of bridging layer in Pond 2, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Overview of Pond 1, looking north.



Overview of Pond 2, looking southwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/2/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Sunny	Temperature: 61
Weather (PM): Sunny	Temperature: 81
Precipitation: None	Wind: W 2-6 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION	
Work performed while Golder was onsite:	
Ryan Central -2 Foreman, 5 Operators, 2 Laborers	
<ul style="list-style-type: none"> Continued placement of bridging layer in Pond 2. Continued regrading of CCR in Pond 2. Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Continue excavating Pond 2's south dike and placing material into Pond 2 for bridging layer. Removed bollards and casing from MW-15005 south of Pond 2 prior to excavating around monitoring well and lowering. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. 	
<u>Summary of Dewatering:</u>	
<u>Week 1</u>	<u>Week 2</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.
<u>Week 3</u>	<u>Week 4</u>
05/20/19: 328,687 gal.	05/27/19: Holiday
05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.
<u>Week 7</u>	<u>Week 8</u>
06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

06/08/19: 65,064 gal. <u>Week 9</u>	06/15/19: 142,063 gal. <u>Week 10</u>	06/22/2019: 102,207 gal. <u>Week 11</u>	06/29/2019: 135,907 gal. <u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in a single layer using CCR in Pond 2.
- Golder observed regrading of CCR in Pond 2.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-34 and SFDT-36 on 9-inch compacted structural fill lift 4 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed excavation of Pond 2's south dike and placement of excavated material into Pond 2 for bridging layer.
- Golder monitored removal of MW-15005 bollards and protective casing prior to removing surrounding CCR and lowering well pipe. Ryan cut well done to about 5 feet above final grade, well to be set at final elevation by sub-contractor after completion of cap.
- Golder observed import of structural fill for Pond 1.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES
None

SUMMARY OF PROBLEMS AND RESOLUTIONS
None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)
None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES
None



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Placement of structural fill in Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Compaction of structural fill placed in Pond 1, looking west.



Removing protective casing from MW-15005, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Removing remaining CCR from around MW-15005, looking northeast.



Excavation of Pond 2's south dike, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/3/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/1530
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Mostly Sunny	Temperature: 63
Weather (PM): Mostly Sunny	Temperature: 83
Precipitation: None	Wind: N 2-5 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Volvo A40 Haul truck; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION	
Work performed while Golder was onsite:	
Ryan Central -1 Foreman, 3 Operators, 2 Laborers	
<ul style="list-style-type: none"> Continued placement of bridging layer in Pond 2. Continued regrading of CCR in Pond 2. Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Removed bollards and casing from MW-15006 south of Pond 2 prior to excavating around monitoring well and lowering. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. 	
<u>Summary of Dewatering:</u>	
<u>Week 1</u>	<u>Week 2</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.
<u>Week 3</u>	<u>Week 4</u>
05/20/19: 328,687 gal.	05/27/19: Holiday
05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.
<u>Week 7</u>	<u>Week 8</u>
06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
 <u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in a single layer using CCR in Pond 2.
- Golder observed regrading of CCR in Pond 2.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-37 and SFDT-39 on 9-inch compacted structural fill lift 5 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder monitored removal of MW-15006 bollards and protective casing prior to removing surrounding CCR and lowering well pipe. Ryan cut well done to about 5 feet above final grade, well to be set at final elevation by sub-contractor after completion of cap.
- Golder observed import of structural fill for Pond 1.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES
None

SUMMARY OF PROBLEMS AND RESOLUTIONS
None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)
None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES
None



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Re-grading of CCR in Pond 2, looking southwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure




Placing 11 inch to 12 inch loose lift of structural fill in Pond 1, looking northeast.



Moisture conditioning of structural fill in Pond 1, looking northeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

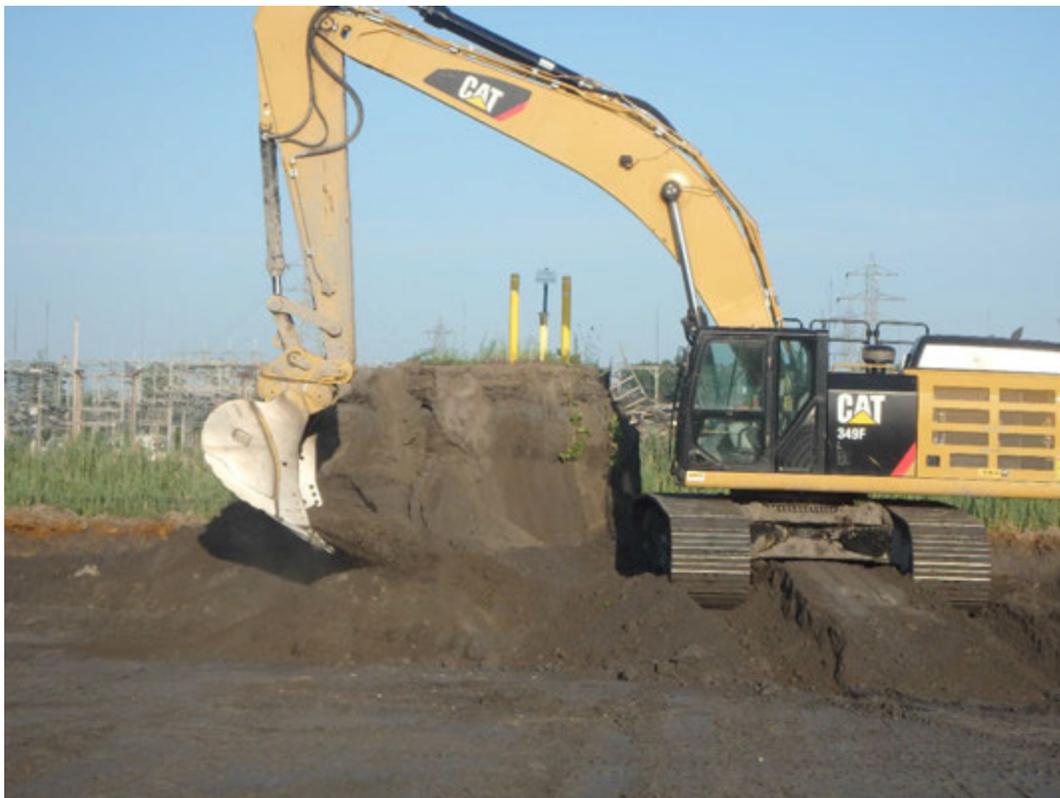

Removing remaining CCR from around MW-15006, looking west.



Overview of Ponds 1 and 2, looking northeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/5/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc. ProAct	Contractor(s) Rep:	John Johnson (Ryan Central) Guillermo Arredondo (ProAct)

SITE CONDITIONS	
Weather (AM): Sunny	Temperature: 66
Weather (PM): Mostly Sunny	Temperature: 89
Precipitation: None	Wind: SE 2-6 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION			
Work performed while Golder was onsite:			
Ryan Central -2 Foreman, 4 Operators, 2 Laborers			
<ul style="list-style-type: none"> Continued placement of bridging layer in Pond 2. Continued regrading of CCR in Pond 2. Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Continued cutting access road east of discharge channel to sub-grade. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. Demobilized Volvo A40G haul truck. 			
ProAct Services – 1 Foreman			
<ul style="list-style-type: none"> ProAct onsite at 0700 to set-up pumps and hoses from Pond 2 to baker tank and discharge channel. 			
<u>Summary of Dewatering:</u>			
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement of bridging layer in a single layer using CCR in Pond 2.
- Golder observed regrading of CCR in Pond 2.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-40 and SFDT-43 on 9-inch compacted structural fill lift 5 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed cutting of the access road east of the discharge channel from Pond 2 to the Chemical Ponds.
- Golder observed import of structural fill for Pond 1.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature: 

PHOTOGRAPHS



Structural fill lift being placed in Pond 1, looking west.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Compaction of placed lift of structural fill in Pond 1, looking west.



Import of structural fill to Pond 1, looking northeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Performing Standard Test prior to start of density testing.



Overview of Pond 2, looking southwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/6/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/1530
Contractor(s):	Ryan Central Inc. ProAct	Contractor(s) Rep:	John Johnson (Ryan Central) Guillermo Arredondo (ProAct)

SITE CONDITIONS	
Weather (AM): Partly Sunny	Temperature: 70
Weather (PM): Overcast	Temperature: 75
Precipitation: Rain	Wind: NW 3-7 mph

EQUIPMENT ON SITE
1-Kubota RTV X112OD; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION																												
Work performed while Golder was onsite:																												
Ryan Central -2 Foreman, 5 Operators, 2 Laborers																												
<ul style="list-style-type: none"> Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Began cutting structural fill placed in Pond 1 to liner finish grade. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. 																												
ProAct Services – 1 Foreman																												
<ul style="list-style-type: none"> ProAct onsite at 0700 to complete set-up of pumps and filter system at Pond 2 																												
<u>Summary of Dewatering:</u>																												
<table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																									
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																									
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																									
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																									
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																									
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																									
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																									

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Structural fill lift being placed in Pond 1, looking west.



Cutting placed and compacted structural fill in Pond 1 to liner sub-grade, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Overview of Pond 1, looking north.



Overview of Pond 2, looking southwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/7/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Mostly Sunny	Temperature: 66
Weather (PM): Partly Sunny	Temperature: 87
Precipitation: None	Wind: SW 0-5 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION	
Work performed while Golder was onsite:	
Ryan Central -2 Foreman, 5 Operators, 1 Laborers	
<ul style="list-style-type: none"> Continued placement of structural fill in Pond 1 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 1 with an 815 compactor. Continued cutting structural fill placed in Pond 1 to liner finish grade. Constructed temporary access road from west gate to Pond 2. Proof rolled section of Pond 2 bridging layer. Structural Fill import for Pond 1. Water truck for dust control and fill moisture. 	
<u>Summary of Dewatering:</u>	
<u>Week 1</u>	<u>Week 2</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.
	<u>Week 3</u>
	05/20/19: 328,687 gal.
	05/21/19: 402,720 gal.
	05/22/19: 487,716 gal.
	05/23/19: 408,516 gal.
	05/24/19: 484,613 gal.
	05/25/19: None
	<u>Week 4</u>
	05/27/19: Holiday
	05/28/19: 386,176 gal.
	05/29/19: 468,094 gal.
	05/30/19: 357,569 gal.
	05/31/19: 161,965 gal.
	06/01/19: None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-44 and SFDT-49 on 9-inch compacted structural fill lift 5 placed in Pond 1 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed cutting of placed, compacted and tested structural fill to liner sub-grade east of grading crest in Pond 1.
- Golder observed construction of temporary access road from west gate to Pond 2 using structural fill.
- Golder monitored proof roll of bridging layer in Pond 2 bounded by certification points; 1057, 1059, 1101 and 1103.
- Golder observed import of structural fill for Pond 1.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

Bi-Weekly construction meeting with CEC, Ryan and Golder representatives.

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Structural fill lift being placed in Pond 1, looking northwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Constructing temp access road to west gate for imports, looking southwest.



Proof rolling of bridging layer in Pond 2.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Overview of Pond 2, looking west.



Structural fill import to Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Composite Proof Roll Map

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/8/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Mostly Sunny	Temperature: 68
Weather (PM): Sunny	Temperature: 83
Precipitation: None	Wind: W 2-13 mph

EQUIPMENT ON SITE
1-Kubota RTV X112OD; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 2-Cat D6T Dozers, 1-John Deere 9520 Tractor

SUMMARY OF CONSTRUCTION	
Work performed while Golder was onsite:	
Ryan Central -1 Foreman, 5 Operators, 1 Laborers	
<ul style="list-style-type: none"> • Began placement of structural fill in Pond 2 in a single 11 to 12 inch loose lift. • Began compacting structural fill placed in Pond 2 with an 815 compactor. • Continued finish grading of structural fill placed in Pond 1. • Structural Fill import for Pond 2. • Import of class 2NS. • Water truck for dust control and fill moisture. 	
<u>Summary of Dewatering:</u>	
<u>Week 1</u>	<u>Week 2</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.
<u>Week 3</u>	<u>Week 4</u>
05/20/19: 328,687 gal.	05/27/19: Holiday
05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/25/19: None	06/01/19: None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder monitored placement of structural fill in Pond 1, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-50 and SFDT-51 on 9-inch compacted structural fill lift 1 placed in Pond 2 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed finish grading structural fill to liner sub-grade in Pond 1.
- Golder observed import of structural fill for Pond 2.
- Golder collected samples of topsoil from Salenbien and Cherry Hill stockpiles for Michigan 10 Metals and BTEX compound/pesticides testing. Samples dropped at Brighton Analytical labs.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

SUBMITTED BY GOLDER:

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

CQA Field Manager: David Hutchinson

Signature: 

PHOTOGRAPHS



Compacting lift of structural fill in Pond 2, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Density testing structural fill lift in Pond 2, looking east.



Overview of Pond 1, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/9/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Sunny	Temperature: 60
Weather (PM): Sunny	Temperature: 82
Precipitation: None	Wind: W 2-9 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION																												
Work performed while Golder was onsite:																												
Ryan Central -1 Foreman, 4 Operators, 1 Laborers																												
<ul style="list-style-type: none"> Continued placement of structural fill in Pond 2 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 2 with an 815 compactor. Continued finish grading of structural fill placed in Pond 1. Proof rolled section of Pond 2 bridging layer. Structural Fill import for Pond 2. Water truck for dust control and fill moisture. Mobilized one Cat TL1055D Tele-Handler. 																												
<u>Summary of Dewatering:</u>																												
<table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																									
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																									
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																									
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																									
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																									
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																									
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																									

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder monitored placement of structural fill in Pond 2, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test SFDT-52 on 9-inch compacted structural fill lift 1 placed in Pond 2 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed finish grading of placed, compacted and tested structural fill Pond 1.
- Golder monitored proof roll of bridging layer in Pond 2 bounded by certification points; 1057, 1056, 1103 and 1104.
- Golder monitored survey of liner sub-grade in Pond 1.
- Golder observed import of structural fill for Pond 2.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

Rowe surveyor shot cert points for liner sub-grade in Pond 1, area surveyed bounded by points; 1000, 1019, 1027 and 1021.

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

Bi-Weekly construction meeting with CEC, Ryan and Golder representatives.

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Survey of certification points for liner sub-grade in Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Maintaining moisture of placed fill, looking west.



Finish grading of liner sub-grade in Pond 1, looking west.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure




Placement of structural fill lift in Pond 2, looking south.



Proof roll of bridging layer in Pond 2, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

DENSITY TEST MAP
LIFT 1

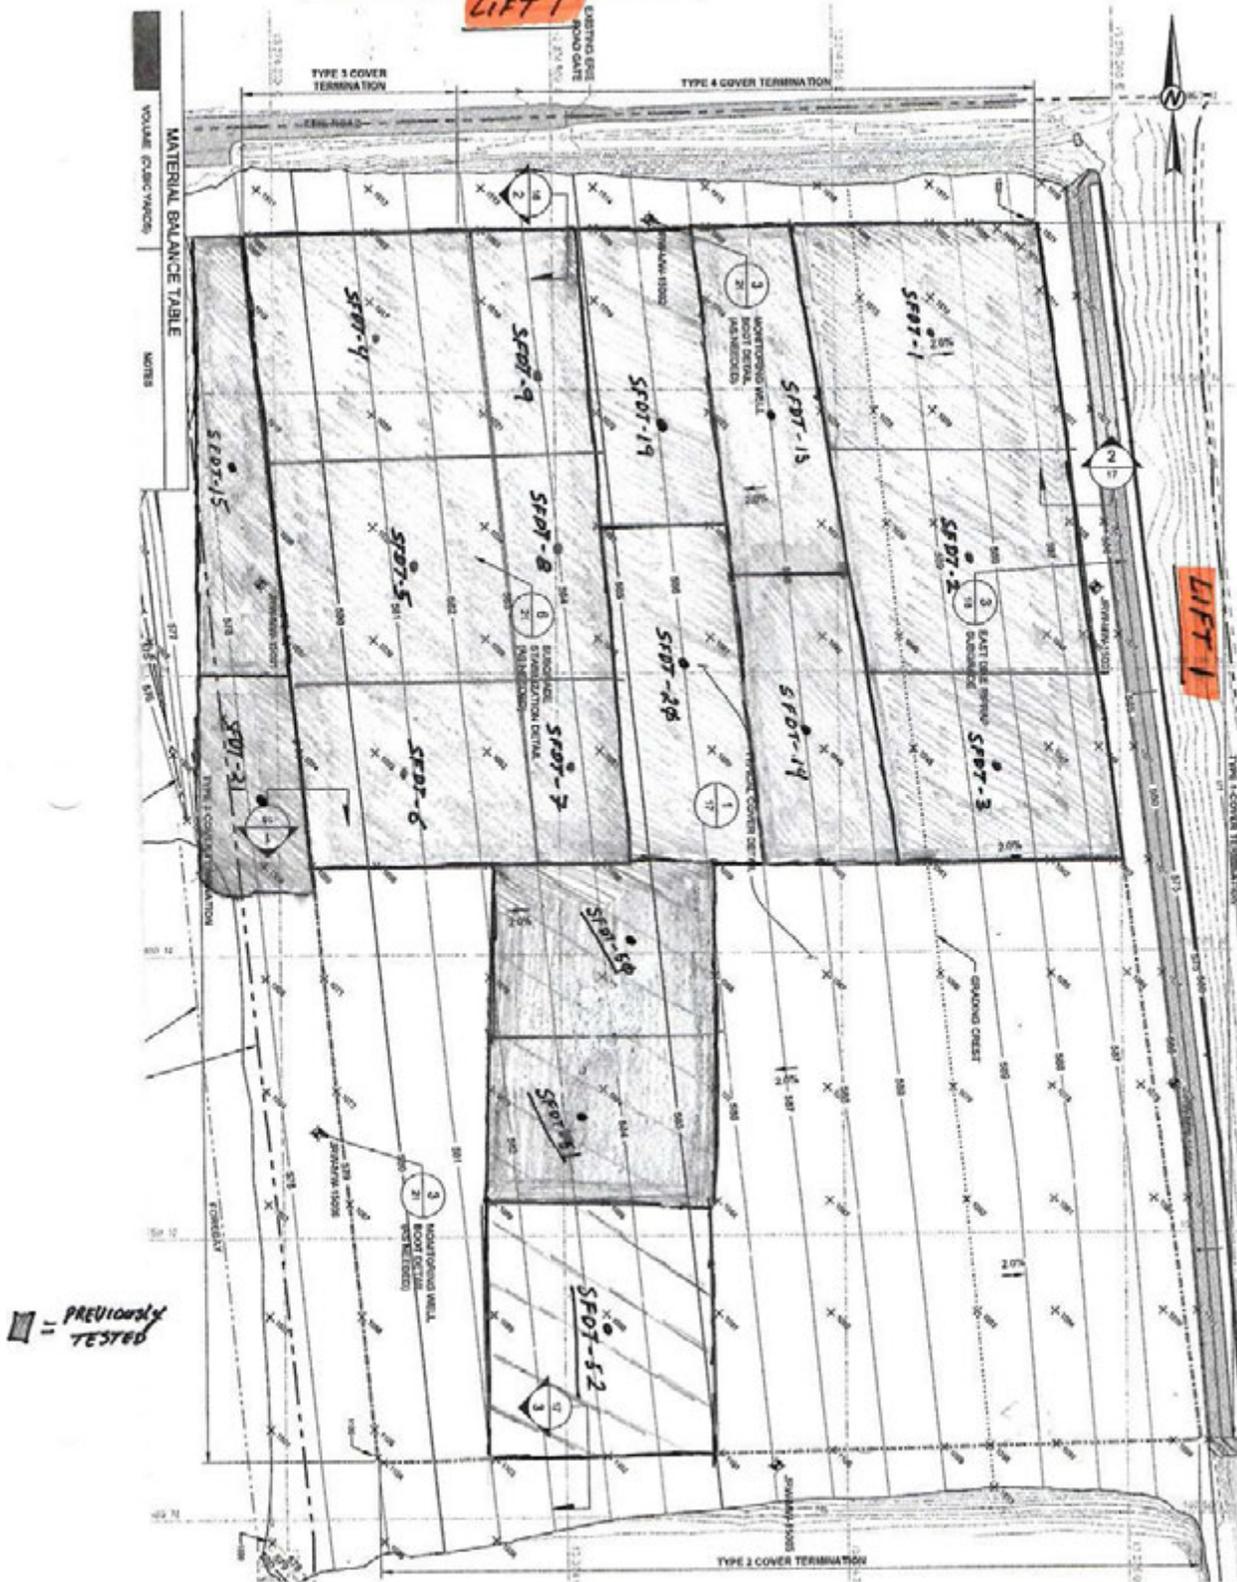

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/10/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/1500
Contractor(s):	Ryan Central Inc.	Contractor(s) Rep:	John Johnson (Ryan Central)

SITE CONDITIONS	
Weather (AM): Partly Sunny	Temperature: 55
Weather (PM): Partly Sunny	Temperature: 75
Precipitation: None	Wind: W 1-6 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION																																																								
Work performed while Golder was onsite:																																																								
Ryan Central -1 Foreman, 4 Operators																																																								
<ul style="list-style-type: none"> Continued finish grading of structural fill placed in Pond 1. Over-Excavated soft spot in Pond 2 bridging layer and backfilled with dry material. Water truck for dust control and fill moisture. 																																																								
<u>Summary of Dewatering:</u>																																																								
<table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table> <table> <thead> <tr> <th><u>Week 5</u></th> <th><u>Week 6</u></th> <th><u>Week 7</u></th> <th><u>Week 8</u></th> </tr> </thead> <tbody> <tr> <td>06/03/19: 185,365 gal.</td> <td>06/10/19: 175,022 gal.</td> <td>06/17/2019: 247,813 gal.</td> <td>06/24/2019: 218,008 gal.</td> </tr> <tr> <td>06/04/19: 409,662 gal.</td> <td>06/11/19: 184,365 gal.</td> <td>06/18/2019: 68,510 gal.</td> <td>06/25/2019: 208,371 gal.</td> </tr> <tr> <td>06/05/19: 345,122 gal.</td> <td>06/12/19: 178,934 gal.</td> <td>06/19/2019: 215,872 gal.</td> <td>06/26/2019: 181,215 gal.</td> </tr> <tr> <td>06/06/19: 311,007 gal.</td> <td>06/13/19: 147,219 gal.</td> <td>06/20/2019: 207,117 gal.</td> <td>06/27/2019: 216,650 gal.</td> </tr> <tr> <td>06/07/19: 276,790 gal.</td> <td>06/14/19: 13,156 gal.</td> <td>06/21/2019: 200,874 gal.</td> <td>06/28/2019: 208,921 gal.</td> </tr> <tr> <td>06/08/19: 65,064 gal.</td> <td>06/15/19: 142,063 gal.</td> <td>06/22/2019: 102,207 gal.</td> <td>06/29/2019: 135,907 gal.</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None	<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>	06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.	06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.	06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.	06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.	06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.	06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																																																					
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																																																					
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																																																					
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																																																					
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																																																					
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																																																					
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																																																					
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>																																																					
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.																																																					
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.																																																					
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.																																																					
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.																																																					
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.																																																					
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.																																																					

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

Week 9	Week 10	Week 11	Week 12
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
Week 13			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed finish grading of placed, compacted and tested structural fill Pond 1.
- Golder observed over-excavation of soft spot found in the bridging layer of Pond 2 during previous day's proof roll. Saturated clay found below the 3 foot bridging layer removed and replaced with dry CCR used for bridging layer.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

While over-ex of soft spot in Pond 2 area to the north was found also to be pumping while excavator was backfilling the over-ex area. Upon further investigation by over-excavating the area found that the material below bridging layer was saturated and not supporting the bridging layer above causing the whole 3 foot layer to pump. After discussion with CEC, Ryan and Golder site reps it was decided to berm off the excavation and discuss further on Monday with CEC and Golder engineers on how to proceed.

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

Bi-Weekly construction meeting with CEC, Ryan and Golder representatives.

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson


Signature: 

PHOTOGRAPHS

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Finish grading structural fill in Pond 1, looking northeast.

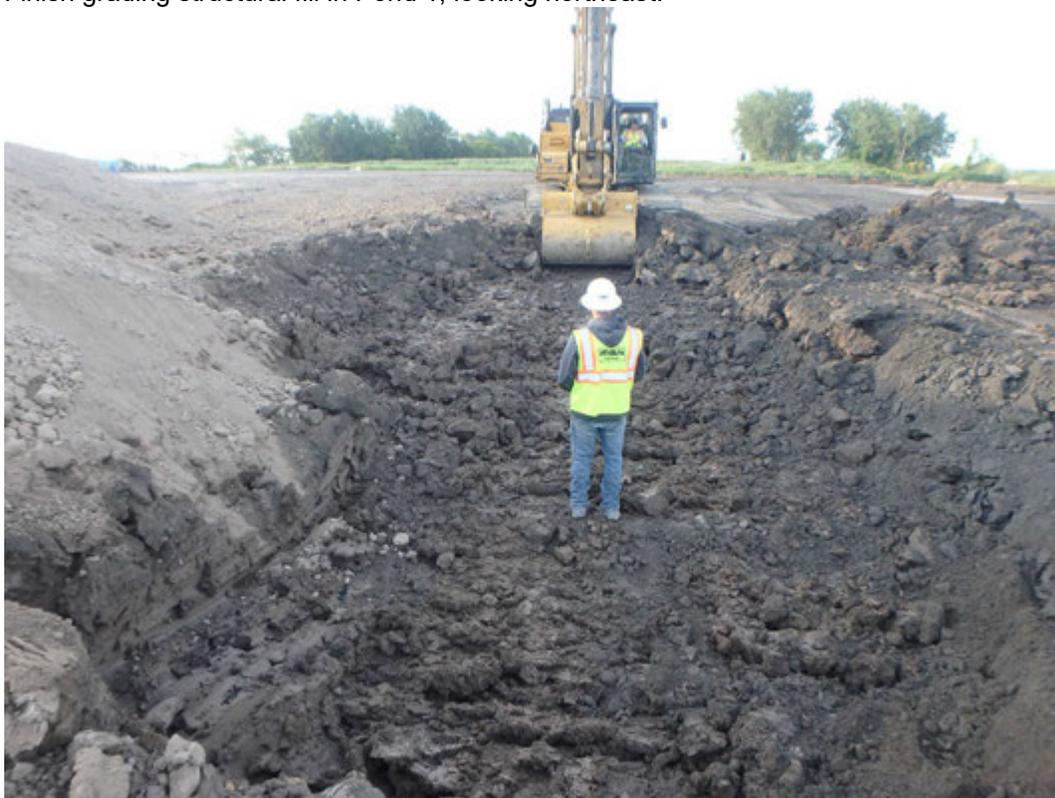

Over-ex of soft spot in bridging layer of Pond 2, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Overview of Pond 1, looking northeast.



Backfill of over-ex in Pond 2, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/12/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc. Chesapeake	Contractor(s) Rep:	John Johnson (Ryan Central) Emiliano Saenz (Chesapeake)

SITE CONDITIONS	
Weather (AM): Mostly Cloudy	Temperature: 69
Weather (PM): Mostly Cloudy	Temperature: 80
Precipitation: None	Wind: SW 0-10 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION			
Work performed while Golder was onsite:			
Ryan Central -1 Foreman, 4 Operators, 1 Laborers			
<ul style="list-style-type: none"> Continued placement of structural fill in Pond 2 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 2 with an 815 compactor. Continued finish grading of structural fill placed in Pond 1. Smooth drum used to roll liner finish grade surveyed for liner deployment. Proof rolled section of Pond 2 bridging layer. Over-Excavated soft area in Pond 2 and backfilled with dry CCR for bridging layer. Structural Fill import for Pond 2. Water truck for dust control and fill moisture. 			
Chesapeake – 1 Superintendent, 12 Technicians, 2 Laborers			
<ul style="list-style-type: none"> Set-up equipment/gear for geomembrane installation. Filling sandbags for liner ballast. 			
<u>Summary of Dewatering:</u>			
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder monitored placement of structural fill in Pond 2, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-53 and 54 on 9-inch compacted structural fill lift 1 placed in Pond 2 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed finish grading of placed, compacted and tested structural fill Pond 1.
- Golder observed rolling liner finish grade surveyed with smooth drum prior to walk-down for final approval to deploy geomembrane.
- Golder monitored proof roll of bridging layer in Pond 2 bounded by certification points; 1059, 1060, 1099.5 and 1101.
- Golder observed over-excavation of soft area in Pond 2, saturated material removed, textile deployed and backfilled with dry CCR.
- Golder observed Chesapeake setting-up equipment/gear.
- Golder observed import of structural fill for Pond 2.
- Golder observed use of water truck for dust control on site.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)
--

Pre-Construction meeting with CEC, Ryan, Chesapeake and Golder covering geomembrane installation.

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES
--

At about 1730 a semi with frameless trailer loaded with structural fill turned over while dumping load. Driver appeared to be uninjured just needing assistance with door on cab to exit the semi. Ryan Central has lead on the accident investigation.

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson
--

Signature:



PHOTOGRAPHS



Proof roll of additional area of Pond 2 bridging layer, looking south.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Smooth drum rolling surveyed liner sub-grade, looking northwest.



Removal of saturated CCR from soft area found while proof rolling in Pond 2, looking southwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Maintaining moisture of placed fill and dust control, looking north.



Overview of Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Composite Proof Roll Map

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/13/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/1600
Contractor(s):	Ryan Central Inc. Chesapeake	Contractor(s) Rep:	John Johnson (Ryan Central) Emiliano Saenz (Chesapeake)

SITE CONDITIONS	
Weather (AM): Mostly Cloudy	Temperature: 70
Weather (PM): Mostly Cloudy	Temperature: 75
Precipitation: Rain	Wind: SW 1-4 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION																												
Work performed while Golder was onsite:																												
Ryan Central -1 Foreman, 3 Operators, 1 Laborers																												
<ul style="list-style-type: none"> Assist with righting of semi with frameless dump that turned over previous workday and clean-up of soil containing fluids that leaked from semi. Received delivery of 4 inch ADS perforated and non-perforated pipe for above-cap drainage system. 																												
Chesapeake – 1 Superintendent, 12 Technicians, 2 Laborers																												
<ul style="list-style-type: none"> Continued set-up equipment/gear for geomembrane installation. Filling sandbags for liner ballast. 																												
<u>Summary of Dewatering:</u>																												
<table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																									
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																									
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																									
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																									
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																									
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																									
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																									

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PHOTOGRAPHS



Dressing access road to Pond 2, looking southeast.



Overview of Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



4 inch ADS pipe for above-cap drainage system.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/14/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2000
Contractor(s):	Ryan Central Inc. Chesapeake	Contractor(s) Rep:	John Johnson (Ryan Central) Emiliano Saenz (Chesapeake)

SITE CONDITIONS	
Weather (AM): Partly Sunny	Temperature: 70
Weather (PM): Mostly Sunny	Temperature: 80
Precipitation: None	Wind: NW 0-9 mph

EQUIPMENT ON SITE
1-Kubota RTV X112OD; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION																												
<p>Work performed while Golder was onsite:</p> <p>Ryan Central -1 Foreman, 3 Operators, 2 Laborers</p> <ul style="list-style-type: none"> Rerouting of access road from west gate. Continued finish grading of liner sub-grade in Pond 1. Proof rolled additional area of Pond 2 bridging layer. Picked rocks from section of liner sub-grade to be approved for deployment. <p>Chesapeake – 1 Superintendent</p> <ul style="list-style-type: none"> No work due to previous night's rain. <p><u>Summary of Dewatering:</u></p> <table> <thead> <tr> <th><u>Week 1</u></th> <th><u>Week 2</u></th> <th><u>Week 3</u></th> <th><u>Week 4</u></th> </tr> </thead> <tbody> <tr> <td>05/06/19: 281,988 gal.</td> <td>05/13/19: 399,021 gal.</td> <td>05/20/19: 328,687 gal.</td> <td>05/27/19: Holiday</td> </tr> <tr> <td>05/07/19: 387,165 gal.</td> <td>05/14/19: 484,537 gal.</td> <td>05/21/19: 402,720 gal.</td> <td>05/28/19: 386,176 gal.</td> </tr> <tr> <td>05/08/19: 405,104 gal.</td> <td>05/15/19: 486,473 gal.</td> <td>05/22/19: 487,716 gal.</td> <td>05/29/19: 468,094 gal.</td> </tr> <tr> <td>05/09/19: 404,705 gal.</td> <td>05/16/19: 481,499 gal.</td> <td>05/23/19: 408,516 gal.</td> <td>05/30/19: 357,569 gal.</td> </tr> <tr> <td>05/10/19: 410,498 gal.</td> <td>05/17/19: 484,331 gal.</td> <td>05/24/19: 484,613 gal.</td> <td>05/31/19: 161,965 gal.</td> </tr> <tr> <td>05/11/19: 64,691 gal.</td> <td>05/18/19: 249,566 gal.</td> <td>05/25/19: None</td> <td>06/01/19: None</td> </tr> </tbody> </table>	<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>	05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday	05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.	05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.	05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.	05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.	05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>																									
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday																									
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.																									
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.																									
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.																									
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.																									
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None																									

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

<u>Week 5</u> 06/03/19: 185,365 gal. 06/04/19: 409,662 gal. 06/05/19: 345,122 gal. 06/06/19: 311,007 gal. 06/07/19: 276,790 gal. 06/08/19: 65,064 gal.	<u>Week 6</u> 06/10/19: 175,022 gal. 06/11/19: 184,365 gal. 06/12/19: 178,934 gal. 06/13/19: 147,219 gal. 06/14/19: 13,156 gal. 06/15/19: 142,063 gal.	<u>Week 7</u> 06/17/2019: 247,813 gal. 06/18/2019: 68,510 gal. 06/19/2019: 215,872 gal. 06/20/2019: 207,117 gal. 06/21/2019: 200,874 gal. 06/22/2019: 102,207 gal.	<u>Week 8</u> 06/24/2019: 218,008 gal. 06/25/2019: 208,371 gal. 06/26/2019: 181,215 gal. 06/27/2019: 216,650 gal. 06/28/2019: 208,921 gal. 06/29/2019: 135,907 gal.
<u>Week 9</u> 07/01/19: 175,586 gal. 07/02/19: 129,459 gal. 07/03/19: 13,878 gal. 07/04/19: None 07/05/19: 137,112 gal. 07/06/19: 95,100 gal.	<u>Week 10</u> 07/08/19: 107,894 gal. 07/09/19: 44,007 gal. 07/10/19: 25,922 gal. 07/11/19: 27,943 gal. 07/12/19: 18,335 gal. 07/13/19: None	<u>Week 11</u> 07/15/19: None 07/16/19: 17,852 gal. 07/17/19: 20,293 gal. 07/18/19: None 07/19/19: 20,316 gal. 07/20/19: None	<u>Week 12</u> 07/22/19: 15,890 gal. 07/23/19: 15,310 gal. 07/24/19: 23,572 gal. 07/25/19: None 07/26/19: None 07/27/19: None
<u>Week 13</u> 07/29/19: None 07/30/19: 23,124 gal. Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed rerouting of west access road to outside of Pond 1 geomembrane limits.
- Golder observed finish grading of Pond 1's liner sub-grade.
- Golder monitored proof roll east side of Pond 2 (see Proof Roll Map below), area rolled passed.
- Golder observed Ryan walk section of Pond 1 bounded by cert points (1000, 1021, 1027 and 1019) prior to sub-grade walk down by CEC, Ryan and Golder for approval to deploy liner.
- Golder performed visual inspection of Pond 1 liner sub-grade with CEC and Ryan representatives.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



PHOTOGRAPHS



Dressing access road to Pond 2, looking southeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Overview of Pond 1, looking southwest.



Proof roll of bridging layer in Pond 2, looking southeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Finish grading Pond 1 liner sub-grade, looking north.



Rolling finish grade in Pond 1, looking southeast.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW

Project Title: J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/15/2019
Client: Consumers Energy	Site/Location: Erie, MI	
GAI Personnel: David Hutchinson	Arrival/Departure Time: 0630/2000	
Contractor(s): Ryan Central Inc. Chesapeake	Contractor(s) Rep: John Johnson (Ryan Central) Emiliano Saenz (Chesapeake)	

SITE CONDITIONS

Weather (AM): Partly Sunny	Temperature: 70
Weather (PM): Mostly Sunny	Temperature: 80
Precipitation: None	Wind: NW 0-9 mph

EQUIPMENT ON SITE

1-Kubota RTV X112OD; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION

Work performed while Golder was onsite:

Ryan Central -1 Foreman, 3 Operators, 2 Laborers

- Continue grading bridging layer in Pond 2.
- Rolled liner sub-grade in Pond 1 with smooth drum roller.
- Continue placement of bridging layer in Pond 2.
- Hauled bottom ash removed from over-excavation in Pond 2 east of certification point 1071 for use in bridging layer.
- Picked rocks from section of liner sub-grade to be approved for deployment.
- Water truck for dust and moisture conditioning of liner sub-grade.

Chesapeake – 1 Superintendent, 11 Technicians, 1 operator, 2 Laborers

- Chesapeake began deployment of geomembrane in Ponds.
- Chesapeake preformed trial welds for fusion and extrusion prior to any seaming or repairs.
- Chesapeake seamed all panels deployed today using the fusion method.
- Chesapeake preformed air pressure testing of all fusion seams to days deployed geomembrane.
- Chesapeake made repairs to all defects on panels P-1 thru P-8 deployed today.
- Chesapeake began vacuum testing of repairs
- Chesapeake field tested destructs DS-1 thru DS-12 marked today.
- Chesapeake placed sandbags around the outside edges of all deployed liner.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

Summary of Dewatering:

<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>			
07/29/19: None			
07/30/19: 23,124 gal.			
Total: 13,861,634 gal.			

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder observed placement and grading of bridging layer in Pond 2.
- Golder observed Ryan walk section of Pond 1 bounded by cert points (1019, 1027, 1037 and 1045) prior to sub-grade walk down by CEC, Ryan and Golder for approval to deploy liner.
- Golder performed visual inspection of Pond 1 liner sub-grade cleared of surface rocks, organics and protrusions bounded by cert points (1019, 1027, 1037 and 1045) with CEC and Ryan representatives, area approved for deployment of geomembrane.
- Golder observed removal of bottom ash from over-excavation east of Pond 2 cert point 1071 and haul for use in bridging layer in Pond 2.
- Performed CQA oversight and documentation on geomembrane installation.
- Performed CQA oversight and documentation on geomembrane installation on Ponds of 40mil HDPE micro-spike geomembrane panels P-1 thru P-12 today.
- Chesapeake installed approximately 111,870sf of geomembrane on Ponds today for a total of 111,870sf to date.
- Golder monitored deployment of 40mil micro-spike geomembrane panels P-1 thru P-8.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

- Golder monitored and documented trial seams for fusion and extrusion in A.M and P.M. performed prior to seaming or repair activities and every 5 hours of operation.
- Golder observed seaming of all deployed panels on Ponds by fusion seaming method using 2 wedges.
- Golder monitored non-destructive testing of all fusion seams by air pressure testing to a minimum of 30psi for 5 minutes with a loss of no more than 4psi in accordance to specifications.
- Golder monitored repairs to geomembrane by extrusion method to install patches in accordance to specifications.
- Golder monitored vacuum testing of repairs.
- Golder marked destructive test locations DS-1 thru DS-12 on geomembrane for removal by Chesapeake and destructive field testing onsite.
- Golder monitored field testing of destructs DS-1 thru DS-12 prior to shipping for third party testing.

SUMMARY OF SURVEYOR'S ACTIVITIES

None

SUMMARY OF PROBLEMS AND RESOLUTIONS
--

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)
--

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES
--

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PHOTOGRAPHS



Deployment of 40mil geomembrane in Pond 1, looking west.




Producing trial weld for field testing.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Testing of trial weld prior to start of seaming.

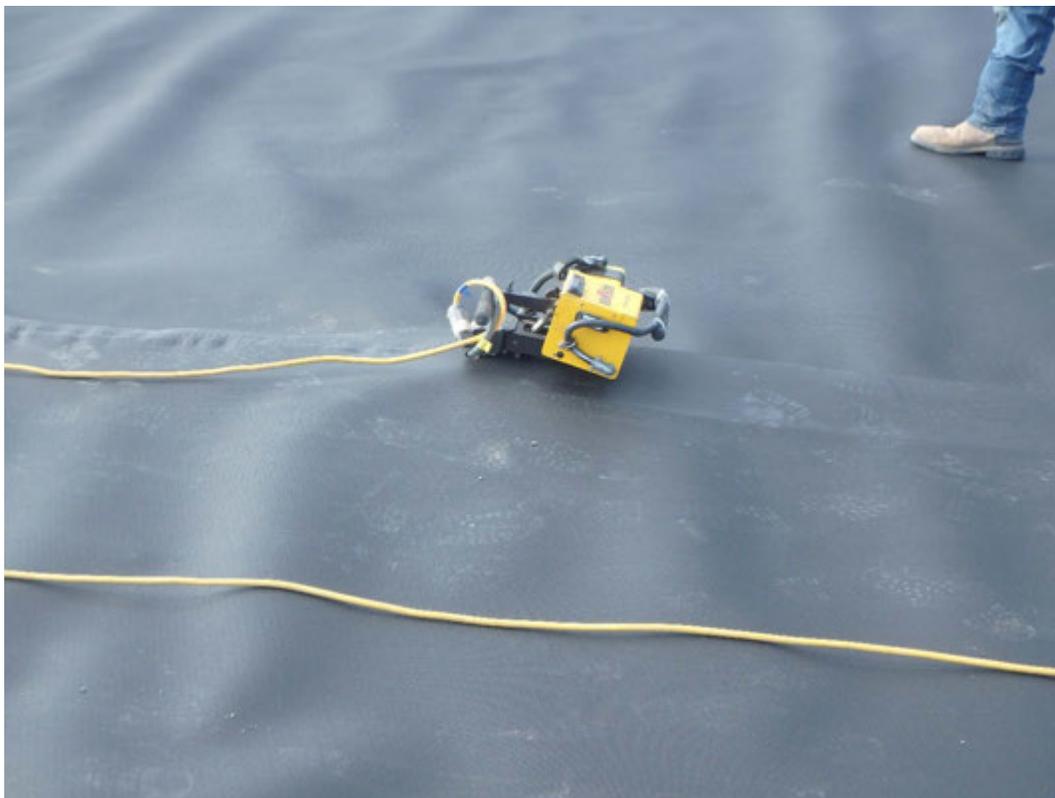

Seaming of geomembrane by fusion method.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Destruct location marked for removal and testing.



Cleaning liner overlap ahead of fusion seaming device.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW			
Project Title:	J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/16/2019
Client:	Consumers Energy	Site/Location:	Erie, MI
GAI Personnel:	David Hutchinson	Arrival/Departure Time:	0630/2030
Contractor(s):	Ryan Central Inc. Chesapeake ProAct	Contractor(s) Rep:	John Johnson (Ryan Central) Emiliano Saenz (Chesapeake) Guillermo Arredondo (ProAct)

SITE CONDITIONS	
Weather (AM): Mostly Cloudy	Temperature: 61
Weather (PM): Mostly Sunny	Temperature: 84
Precipitation: None	Wind: W 0-12 mph

EQUIPMENT ON SITE
1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION
<p>Work performed while Golder was onsite:</p> <p>Ryan Central -1 Foreman, 4 Operators, 2 Laborers</p> <ul style="list-style-type: none"> Continued placement of structural fill in Pond 2 in a single 11 to 12 inch loose lift. Continued compacting structural fill placed in Pond 2 with an 815 compactor. Continued finish grading of structural fill placed in Pond 1. Began installation of French Drain to dewater soft area in Pond 2. Rolled liner sub-grade in Pond 1 with smooth drum roller. Picked rocks from section of liner sub-grade to be approved for deployment. Import structural fill. Water truck for dust and moisture conditioning of liner sub-grade. <p>ProAct Services – 1 Foreman</p> <ul style="list-style-type: none"> ProAct onsite at 0900 to pump baker tanks to discharge channel. Turbidity readings were taken by ProAct while pumping to discharge channel and licensed tester onsite in A.M. <p>Chesapeake – 1 Superintendent, 11 Technicians, 1 operator, 2 Laborers</p> <ul style="list-style-type: none"> Chesapeake continued deployment of geomembrane in Pond 1. Chesapeake preformed trial welds for fusion prior to any seaming. Chesapeake seamed all panels deployed today using the fusion method. Chesapeake preformed air pressure testing of all fusion seams performed today on deployed geomembrane.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

- Chesapeake continued vacuum testing of repairs
- Chesapeake began deployment of geotextile above geomembrane.
- Chesapeake sewed all geotextile seams on geotextile panels placed today.
- Chesapeake placed sandbags around the outside edges of all deployed liner.

Summary of Dewatering:

<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>	<u>Week 14</u>		
07/29/19: None	08/16/19: 49,780		
07/30/19: 23,124 gal.	Total: 13,911,414 gal.		

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder monitored placement of structural fill in Pond 2, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-55 thru 61 on 9-inch compacted structural fill lift's 1 thru 3 placed in Pond 2 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder observed finish grading of placed, compacted and tested structural fill Pond 1.
- Golder observed rolling liner finish grade surveyed with smooth drum prior to walk-down for final approval to deploy geomembrane.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

- Golder observed Ryan walk section of Pond 1 bounded by cert points (1037, 1045, 1046 and 1055) prior to sub-grade walk down by CEC, Ryan and Golder for approval to deploy liner.
- Golder performed visual inspection of Pond 1 liner sub-grade cleared of surface rocks, organics and protrusions bounded by cert points (1037, 1045, 1046 and 1055) with CEC and Ryan representatives, area approved for deployment of geomembrane.
- Golder observed installation of a French Drain in Pond 2 to dewater soft area found during proof roll.
- Performed CQA oversight and documentation on geomembrane installation.
- Performed CQA oversight and documentation on 40mil HDPE micro-spike geomembrane and 8oz. geotextile installed today.
- Chesapeake installed approximately 142,560sf of geomembrane on Ponds today for a total of 254,430sf to date.
- Golder monitored deployment of 40mil micro-spike geomembrane panels P-9 thru P-17.
- Golder monitored and documented trial seams for fusion in A.M and P.M. performed prior to seaming activities and every 5 hours of operation.
- Golder observed seaming of all deployed panels on Ponds by fusion seaming method using 3 wedges.
- Golder monitored non-destructive testing of all fusion seams by air pressure testing to a minimum of 30psi for 5 minutes with a loss of no more than 4psi in accordance to specifications.
- Golder monitored vacuum testing of repairs.
- Golder marked destructive test locations DS-13 thru DS-26 on geomembrane for removal by Chesapeake and destructive field testing onsite.
- Golder observed deployment of 8oz. geotextile above geomembrane.
- Golder observed all seams of geotextile sewn in accordance to specifications.

SUMMARY OF SURVEYOR'S ACTIVITIES

Rowe onsite to shoot additional area of liner sub-grade in Pond 1 bounded by certification points 1037, 1045, 1046 and 1055.

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PHOTOGRAPHS



Deployment of 8oz. geotextile in Pond 1, looking west.



Sewing geotextile seam.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Overview of geomembrane deployed in Pond 1, looking west.



Seaming of geomembrane by fusion method.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Structural fill import to Pond 2, looking west.



French drain in Pond 2, looking east.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

S.F. LIFT MAP / LIFT 2



MATERIAL BALANCE TABLE
VOLUME (CUBIC YARDS)
NOTES




DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

DENSITY TEST MAP LIFT 2

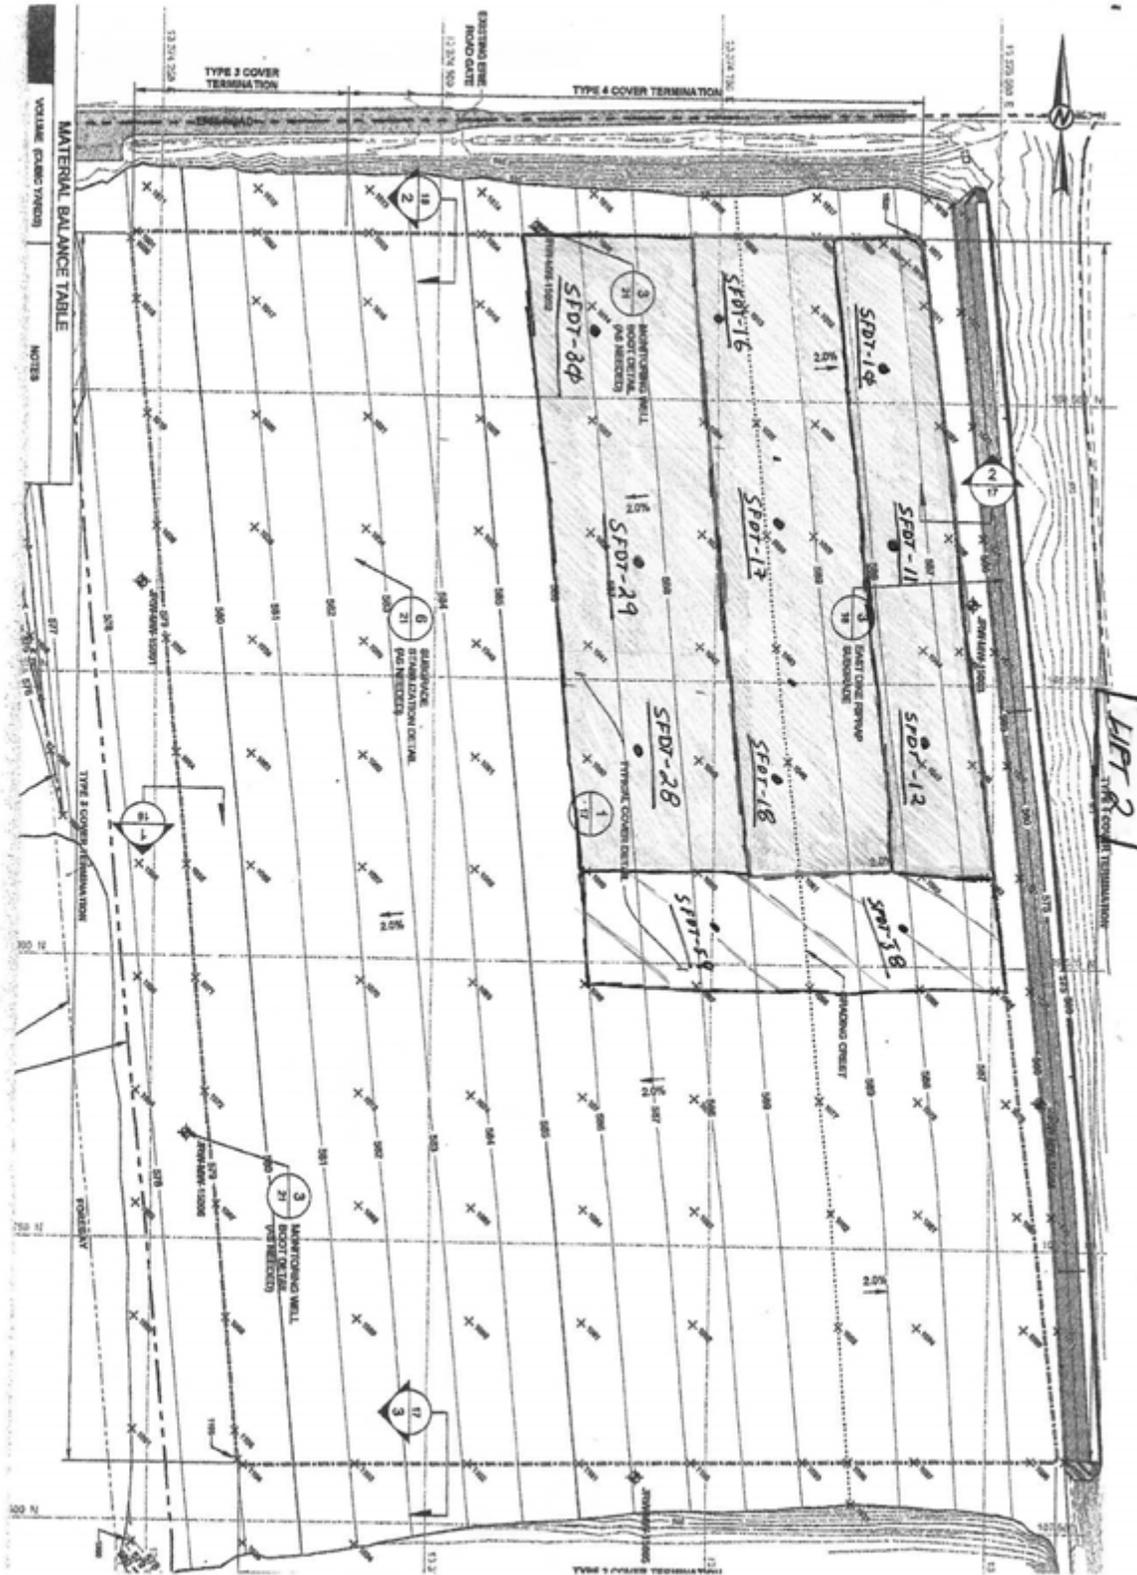

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PROJECT OVERVIEW

Project Title: J.R. Whiting Ponds 1 and 2 Closure CQA	Project Number: 1788523	Date: 8/17/2019
Client: Consumers Energy	Site/Location: Erie, MI	
GAI Personnel: David Hutchinson	Arrival/Departure Time: 0630/1730	
Contractor(s): Ryan Central Inc. Chesapeake ProAct	Contractor(s) Rep: John Johnson (Ryan Central) Emiliano Saenz (Chesapeake) Guillermo Arredondo (ProAct)	

SITE CONDITIONS

Weather (AM): Partly Sunny	Temperature: 68
Weather (PM): Mostly Cloudy	Temperature: 82
Precipitation: None	Wind: W 3-9 mph

EQUIPMENT ON SITE

1-Kubota RTV X1120D; 1-CAT Water Truck; 1-CAT 349F Excavator; 1-CAT A200 LGP Dozer; 1-John Deere 644G Loader; 1-Cat CS56B Smooth Drum Roller; 1-Cat D6T Dozers, 1-John Deere 9520 Tractor, 1-Cat TL1055D Tele-Handler

SUMMARY OF CONSTRUCTION

Work performed while Golder was onsite:

Ryan Central -1 Foreman, 3 Operators, 2 Laborers

- Continued placement of structural fill in Pond 2 in a single 11 to 12 inch loose lift.
- Continued compacting structural fill placed in Pond 2 with an 815 compactor.
- Completed installation of French Drain to dewater soft area in Pond 2.
- Proof roll of bridging layer in Pond 2.
- Rolled liner sub-grade in Pond 1 with smooth drum roller.
- Import structural fill.
- Water truck for dust and moisture conditioning of liner sub-grade.

ProAct Services – 1 Foreman

- ProAct onsite at 0900 to check baker tanks.

Chesapeake – 1 Superintendent, 11 Technicians, 1 operator, 2 Laborers

- Chesapeake continued deployment of geomembrane in Pond 1.
- Chesapeake preformed trial welds for fusion and extrusion prior to any seaming or repairs.
- Chesapeake seamed all panels deployed today using the fusion method.
- Chesapeake preformed air pressure testing of all fusion seams performed today on deployed geomembrane.
- Chesapeake made repairs to all defects on panels P-9 thru P-22 deployed.
- Chesapeake continued vacuum testing of repairs

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

- Chesapeake placed sandbags around the outside edges of all deployed liner.

Summary of Dewatering:

<u>Week 1</u>	<u>Week 2</u>	<u>Week 3</u>	<u>Week 4</u>
05/06/19: 281,988 gal.	05/13/19: 399,021 gal.	05/20/19: 328,687 gal.	05/27/19: Holiday
05/07/19: 387,165 gal.	05/14/19: 484,537 gal.	05/21/19: 402,720 gal.	05/28/19: 386,176 gal.
05/08/19: 405,104 gal.	05/15/19: 486,473 gal.	05/22/19: 487,716 gal.	05/29/19: 468,094 gal.
05/09/19: 404,705 gal.	05/16/19: 481,499 gal.	05/23/19: 408,516 gal.	05/30/19: 357,569 gal.
05/10/19: 410,498 gal.	05/17/19: 484,331 gal.	05/24/19: 484,613 gal.	05/31/19: 161,965 gal.
05/11/19: 64,691 gal.	05/18/19: 249,566 gal.	05/25/19: None	06/01/19: None
<u>Week 5</u>	<u>Week 6</u>	<u>Week 7</u>	<u>Week 8</u>
06/03/19: 185,365 gal.	06/10/19: 175,022 gal.	06/17/2019: 247,813 gal.	06/24/2019: 218,008 gal.
06/04/19: 409,662 gal.	06/11/19: 184,365 gal.	06/18/2019: 68,510 gal.	06/25/2019: 208,371 gal.
06/05/19: 345,122 gal.	06/12/19: 178,934 gal.	06/19/2019: 215,872 gal.	06/26/2019: 181,215 gal.
06/06/19: 311,007 gal.	06/13/19: 147,219 gal.	06/20/2019: 207,117 gal.	06/27/2019: 216,650 gal.
06/07/19: 276,790 gal.	06/14/19: 13,156 gal.	06/21/2019: 200,874 gal.	06/28/2019: 208,921 gal.
06/08/19: 65,064 gal.	06/15/19: 142,063 gal.	06/22/2019: 102,207 gal.	06/29/2019: 135,907 gal.
<u>Week 9</u>	<u>Week 10</u>	<u>Week 11</u>	<u>Week 12</u>
07/01/19: 175,586 gal.	07/08/19: 107,894 gal.	07/15/19: None	07/22/19: 15,890 gal.
07/02/19: 129,459 gal.	07/09/19: 44,007 gal.	07/16/19: 17,852 gal.	07/23/19: 15,310 gal.
07/03/19: 13,878 gal.	07/10/19: 25,922 gal.	07/17/19: 20,293 gal.	07/24/19: 23,572 gal.
07/04/19: None	07/11/19: 27,943 gal.	07/18/19: None	07/25/19: None
07/05/19: 137,112 gal.	07/12/19: 18,335 gal.	07/19/19: 20,316 gal.	07/26/19: None
07/06/19: 95,100 gal.	07/13/19: None	07/20/19: None	07/27/19: None
<u>Week 13</u>	<u>Week 14</u>		
07/29/19: None	08/16/19: 49,780		
07/30/19: 23,124 gal.	Total: 13,911,414 gal.		

GAI CQA ACTIVITIES AND TEST RESULTS

Construction:

- Golder onsite documenting the construction progress.
- Golder monitored placement of structural fill in Pond 2, Cat D6T with GPS placed material in a single 11 to 12 inch loose lift. Cat 815 sheep foot was used to compact to 9 inches.
- Golder performed Standard test on Troxler 3440 prior to density testing.
- Performed density test's SFDT-62 thru 65 on 9-inch compacted structural fill lift's 2 and 3 placed in Pond 2 using a Troxler 3440 Nuclear Gauge (see density test map). Compacted and tested structural fill met all specifications.
- Golder monitored proof roll along west side of Pond 2 using Cat water truck.
- Golder observed installation of a French Drain in Pond 2 to dewater soft area found during proof roll.
- Performed CQA oversight and documentation on geomembrane installation.
- Performed CQA oversight and documentation on 40mil HDPE micro-spike geomembrane installed today.
- Chesapeake installed approximately 79,200sf of geomembrane on Ponds today for a total of 333,630sf to date.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

- Golder monitored deployment of 40mil micro-spike geomembrane panels P-18 thru P-22.
- Golder monitored and documented trial seams for fusion and extrusion in A.M and P.M. performed prior to seaming or repair activities and every 5 hours of operation.
- Golder observed seaming of all deployed panels on Ponds by fusion seaming method using 3 wedges.
- Golder monitored non-destructive testing of all fusion seams by air pressure testing to a minimum of 30psi for 5 minutes with a loss of no more than 4psi in accordance to specifications.
- Golder observed repairs to defects by extrusion method.
- Golder monitored vacuum testing of repairs.
- Golder marked destructive test locations DS-27 thru DS-33 on geomembrane for removal by Chesapeake and destructive field testing onsite.
- Golder monitored field testing of destructs DS-13 thru DS-33 prior to shipping for third party testing.

SUMMARY OF SURVEYOR'S ACTIVITIES

Rowe onsite to shoot additional area of liner sub-grade in Pond 1 bounded by certification points 1037, 1045, 1046 and 1055.

SUMMARY OF PROBLEMS AND RESOLUTIONS

None

SUMMARY OF MEETINGS/DISCUSSIONS HELD (ATTENDEES AND ISSUES)

None

SUMMARY OF INCIDENTS / ACCIDENTS / HEALTH AND SAFETY ISSUES

None

SUBMITTED BY GOLDER:

CQA Field Manager: David Hutchinson

Signature:



DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

PHOTOGRAPHS



Placing structural fill lift in Pond 2, looking southwest.



Deploying geomembrane in Pond 1, looking north.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure



Seaming by fusion method of geomembrane.



Fusion trial weld.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure




Field testing of destructs.



Preparing to deploy liner, looking northwest.

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

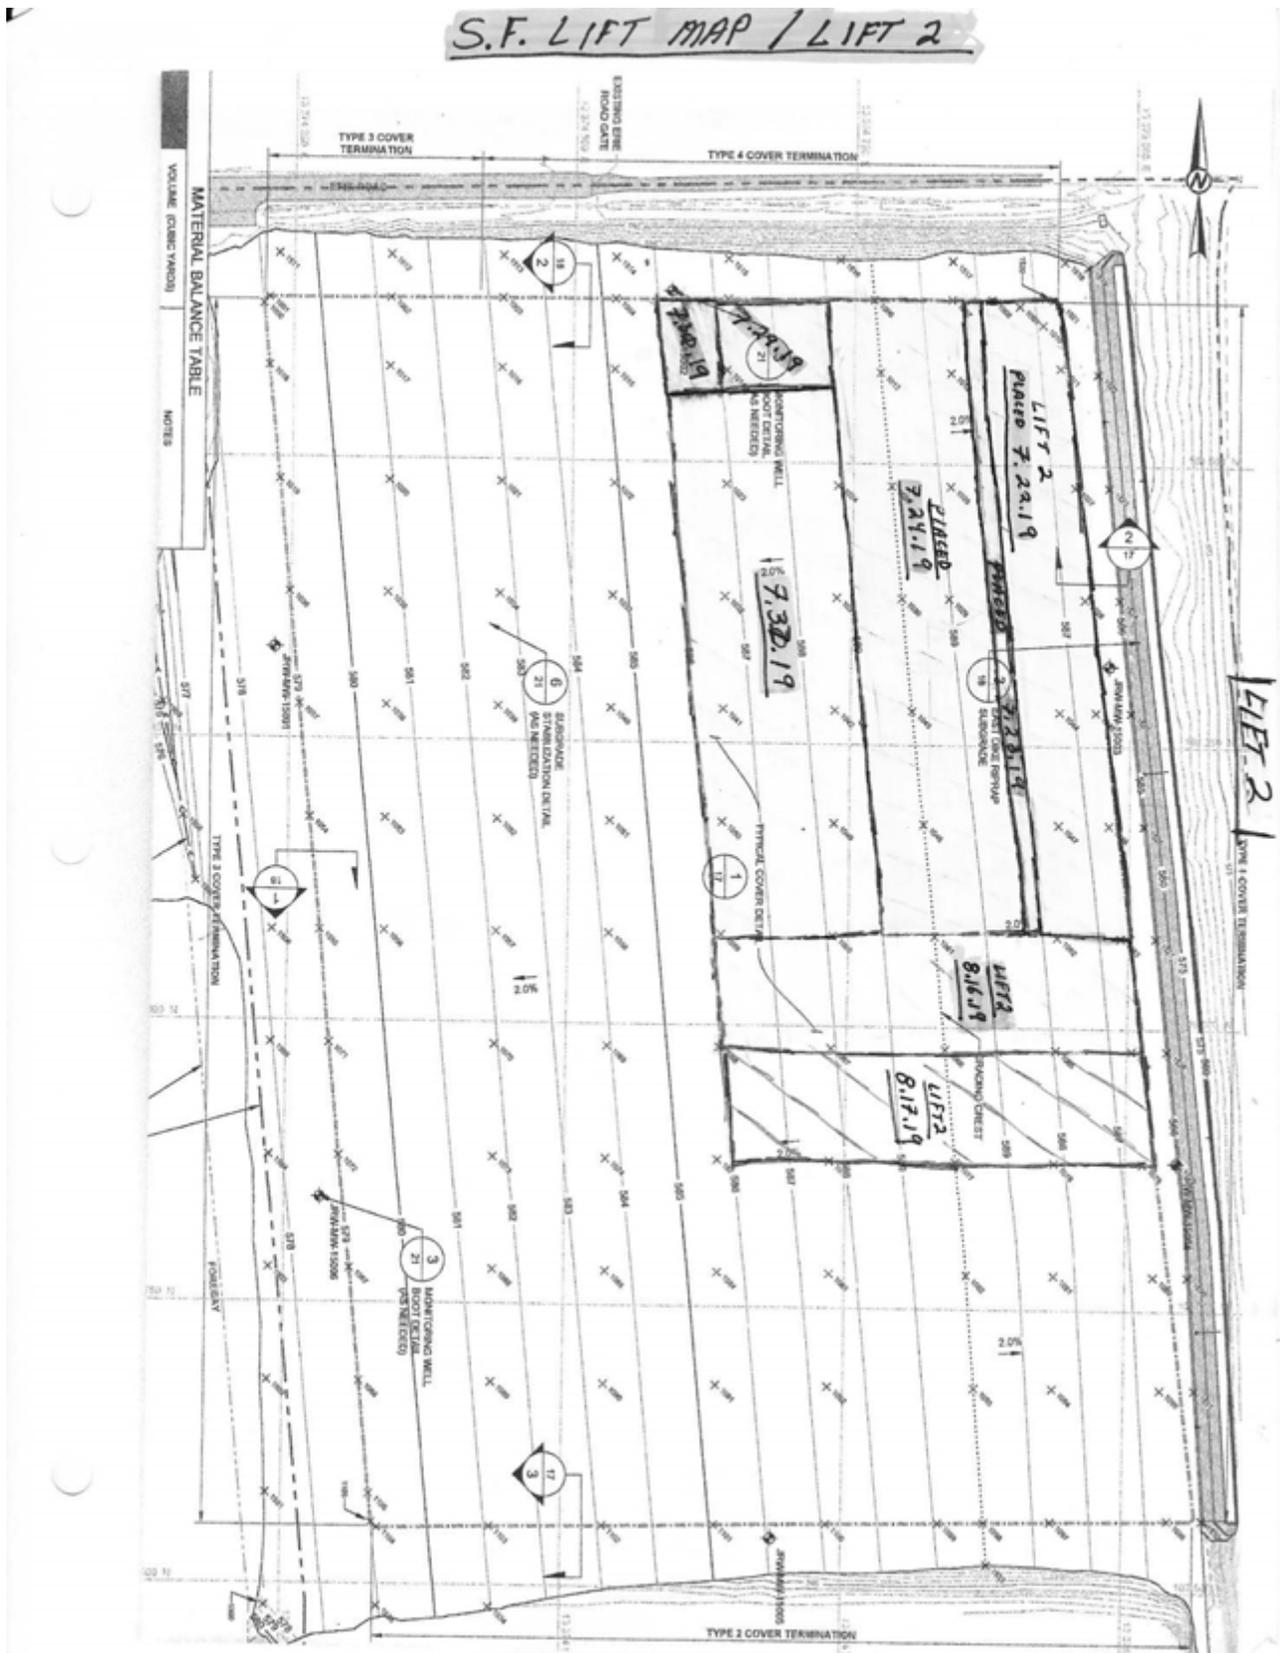

DAILY FIELD FORM – J.R. Whiting Ponds 1 and 2 Closure

DENSITY TEST MAP LIFT 2

